

AI 内容交付平台验证项目

项目按计划进入真实用户验证，但商业证据仍需在 6 周内补齐

批准继续 6 周验证期，暂不进入规模化建设

Dashboard

status and risks

Roadmap

phase plan

Decision

recommended path

Tracker

owners and dates

项目总体健康度：工程按计划推进，商业证据仍需补齐

工程闭环已可运行；当前管理重点是用户成功率、付费意愿和范围控制。

Overall:
YELLOW

Schedule

88%
P0 工作流按计划推进

Budget

+6%
渲染与媒体成本需监控

Scope

Stable
暂不扩视频与团队协作

Risk

Med
市场验证尚未完成

Quality

92%
PPTX QA 与回读通过

Risk	Impact	Owner	Mitigation	Status
真实用户留存不足	High	PM	每周 2 次真实任务回访	yellow
范围扩张过快	High	Product	变更进入 Go/No-Go 会议	red
外部发布接口失败	Medium	Engineering	保留人工交接与回执日志	yellow

Next actions

- 锁定 10 位种子用户名单
- 建立每周真实交付回执表
- 完成付费意愿访谈脚本
- 冻结 P0 以外功能

路线图不是甘特图：用阶段、目标和门禁表达管理节奏



Management rule: every phase ends with a decision gate, not a feature-complete declaration.

里程碑页把时间点、证据和状态压到一条水平轴上



Milestone discipline: dates are only useful when paired with evidence, owner, and decision consequence.

RAID 页优先做成可查表格，避免把风险画成装饰图

Type	Item	Impact	Owner	Mitigation	Status
Risk	P0 价值不够高频	High	PM	只统计真实交付回执	yellow
Assumption	AI 重度创作者愿为稳定交付付费	High	Growth	第 4 周完成定价访谈	gray
Issue	外部接口授权会中断自动化	Medium	Engineering	建立人工接管 SOP	yellow
Dependency	公众号草稿接口稳定性	Medium	Ops	用本地稿件与回执兜底	green

RAID governance check Each row must have a type, owner, mitigation path, and current status. Empty owner or mitigation fields fail PMO QA.

workflows use swimlanes to express responsibility boundaries, rather than task lists



RACI 是精确查阅页：角色和责任必须保持表格可编辑

Task	PM	Eng	Design	Ops	Sponsor
Define pilot scope	A	C	C	R	I
Build editable deck pack	C	R	A	I	I
Recruit seed users	C	I	I	R	A
Run weekly review	A	C	C	R	I
Go / No-Go decision	R	C	C	I	A

R

Responsible

A

Accountable


C

Consulted

I

Informed

风险热力图是坐标页：影响和可能性必须能被复核

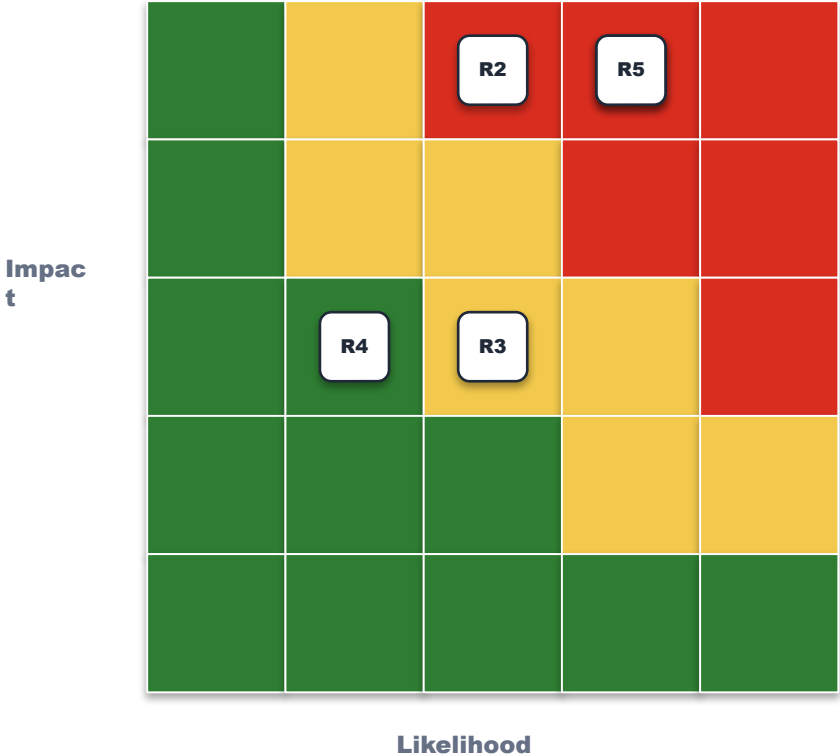

ID	Risk	Owner	I	L
R1	低频使用	PM	5	4
R2	范围失控	PM	5	3
R3	接口失败	Eng	3	3
R4	成本超标	Ops	3	2
R5	付费意愿弱	Growth	5	4

PMO QA: all risk coordinates must be 1-5 and every point must have an owner.

决策页必须给出选项、权衡和推荐，而不是只列利弊

是否批准进入 6 周 PMO 专业包验证？

A. 停止投入

Score 2/5

Pros

- 节省短期资源

Cons

- 错失付费生产包窗口
- 无法验证真实客户需求

B. 有条件验证

Score 5/5

Pros

- 控制范围
- 获得真实数据
- 保留商业化机会

Cons

- 需要每周复盘
- 短期仍有交付成本

C. 直接规模化

Score 1/5

Pros


- 速度最快

Cons

- 无留存与付费证据
- 范围和成本风险高

推荐 B：批准 6 周验证期，未达门槛则停止扩张。

KPI Dashboard 用大数字和一张原生图表支撑管理判断

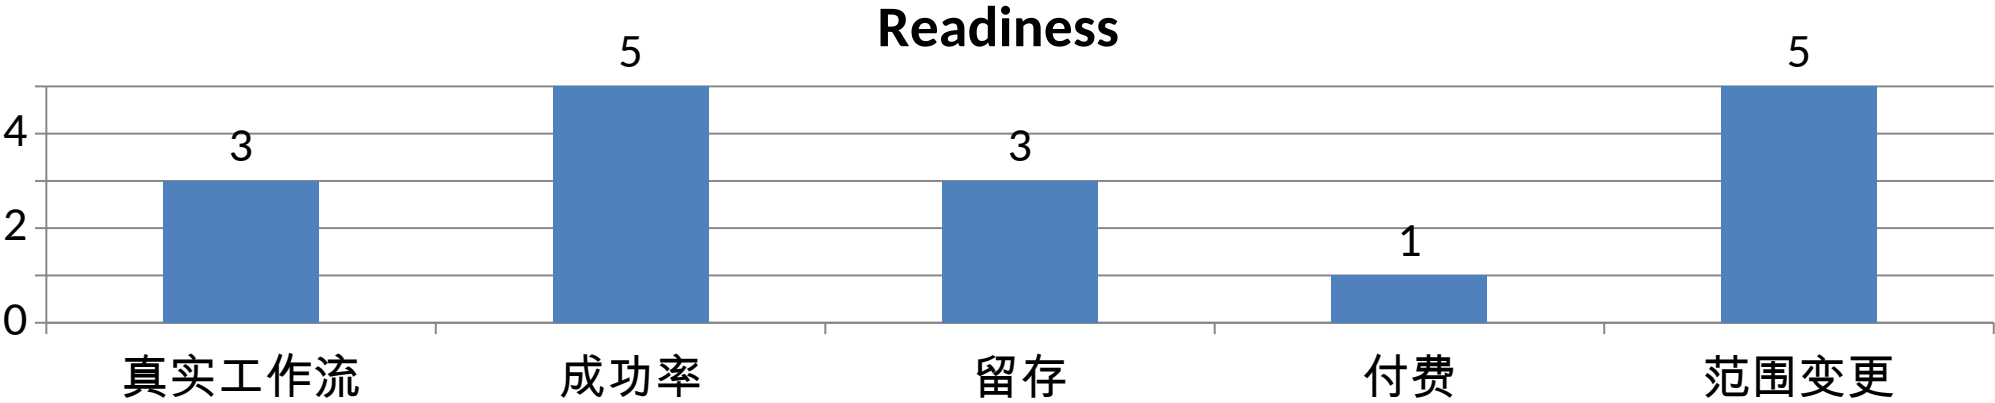

行动项追踪页像 Excel ，但必须有清晰 owner、 deadline 和 status

Owner	Action	Deadline	Status
PM	确认 10 位种子用户与任务类型	07/26	yellow
Eng	完成 PMO renderer v0.1 验收	07/24	green
Design	定义 10 类页面视觉规格	07/25	yellow
Ops	建立真实交付回执表	07/27	gray
Sponsor	确认 6 周 Go/No-Go 门槛	07/28	yellow

Next review: update status before the weekly PMO meeting; overdue red rows require a mitigation owner.
